




Thursday, 22 February

## Project: Albury Street Asphalt Project - PROGRAM update

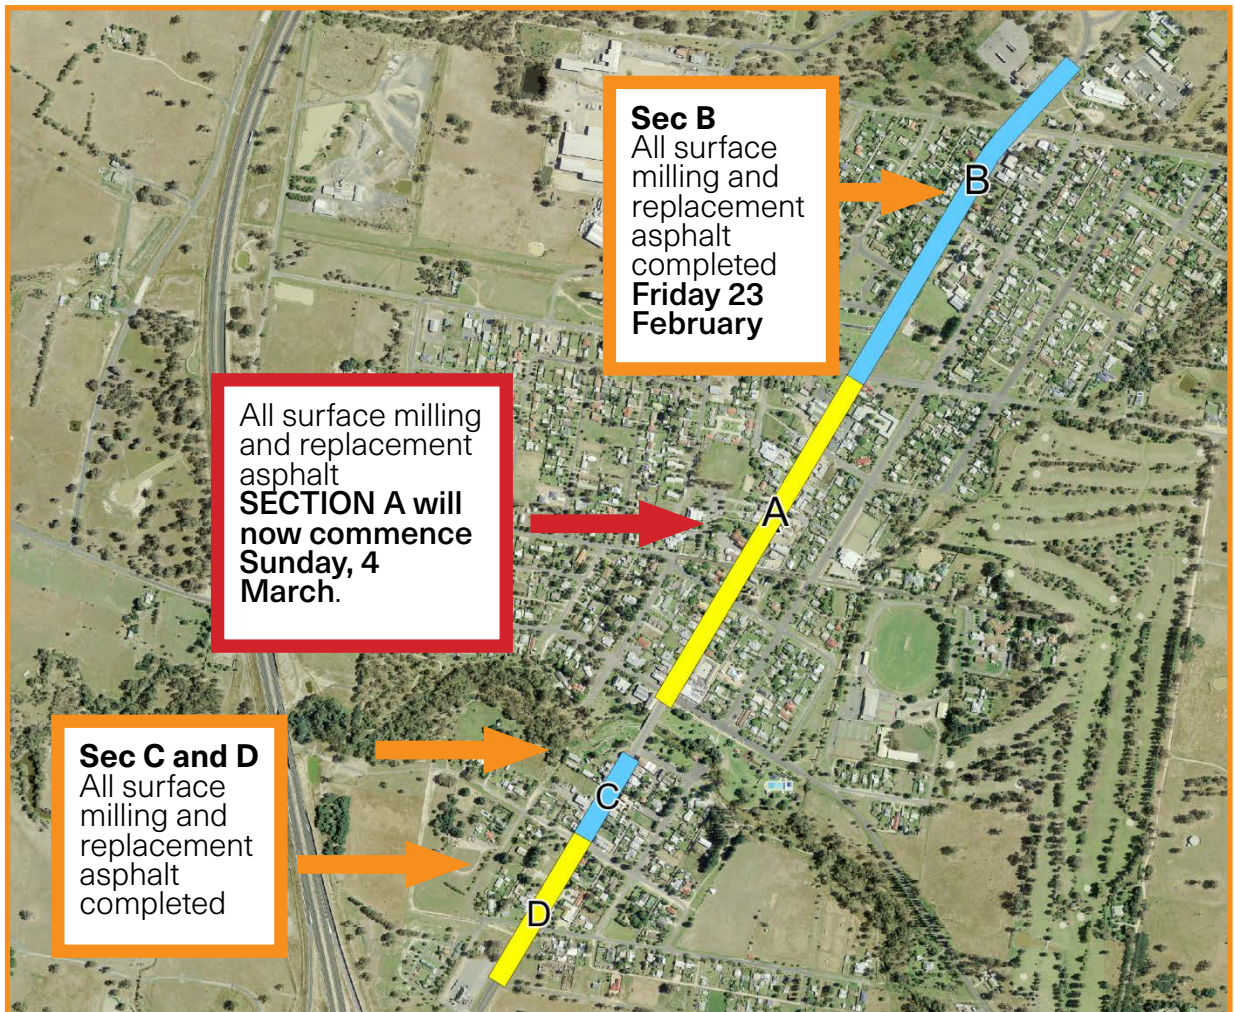

Bitumen resurfacing of Albury Street, Holbrook Sections B, C and D are completed as of COB Friday, 23 February.

Due to circumstances outside of Council's control, the works proposed for SECTION A have today been postponed for one week.

### For more information

- Phil McDonald M 0429 120 083
- Ken Thompson M 0438 777 433
- Dwayne Hartwick (Downer EDI) M 0467 749 675

**Works to be undertaken in Section A will now commence Sunday, 4 March with milling of the existing surface.**

**The laying of asphalt will take 3 to 4 days and be finished by end of Thursday, 8 March.**

### Revised timetable\*

#### Sunday, 4 March 2018

Section A milling of existing surface

#### Monday, 5 March

Section A asphalt surface installation starts

#### Thursday, 8 March

Section A works conclude.

\* Timetable is subject to weather conditions.
